
CLEAR LAKE WATERMAIN AND STORM SEWER PHASE 1A

PROJECT DESCRIPTION

This project consists of watermain and storm sewer improvements, complete street reconstruction including curb & gutter and asphalt pavement, new driveway approach pavement, pedestrian ramp and sidewalk replacement and various removals related to construction of the utilities and street reconstruction.

PROJECT UPDATE | September 21st, 2026



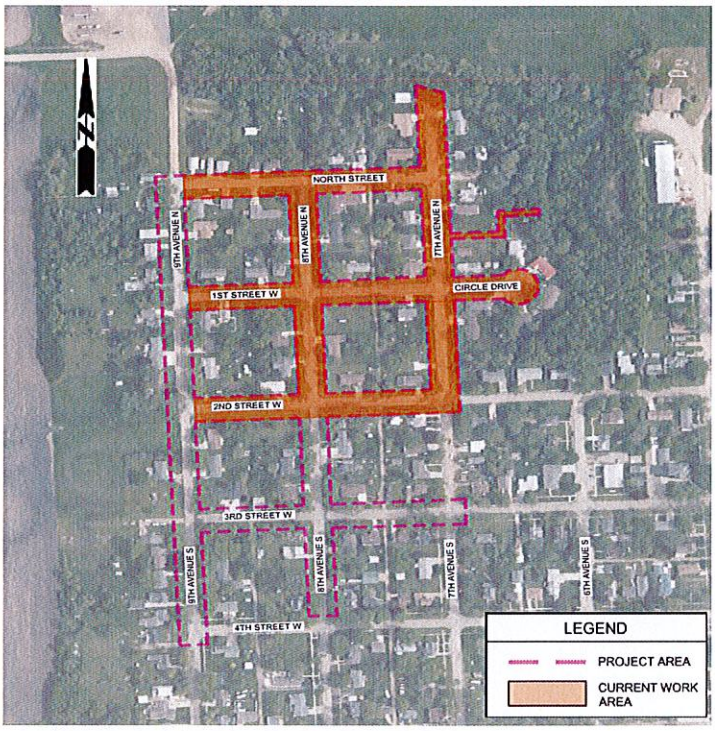

PROJECT INFORMATION

CONSULTANT:

Name: Banner Associates, Inc.
Address: 409 22nd Avenue S, Brookings SD
Phone: 605.692.5714
CONTACT: Landen Buse, Ryan Engstrom, and Scot Leddy

CONTRACTOR:

Name: AP & Sons Construction, Inc
Address: 212 South 6th Street, Milbank SD
Phone 605.520.6647
CONTACT: Justin Eccles

OWNER:

Name: City of Clear Lake
Address: 125 3rd Avenue S, Clear Lake SD
Phone: 605.881.8056
CONTACT: Elliott Furman

PROJECT UPDATE AND SCHEDULE

AP & Sons completed watermain tie-in on 1st Street between 8th Avenue and 7th Avenue. Pressure test and water quality (bacteria) testing are completed and met the requirements of drinking water safety standards. They also continued working on grading the 2nd Street between 9th Avenue and 7th Avenue, and 1st from 8th Avenue to 7th Avenue in preparation for cement treated sub-grade, which is planned for Monday, September 21st depending on weather.

Concrete crew continued curb and gutter installation, they will be installing curb and gutter in Circle Dr the week of the 21st and proceed with fillet and valley gutter installation.

REMINDER: Residents without alley access can expect temporary restrictions to driveway access while the newly installed curb and gutter cures. Please use adjacent streets for parking during this time.

If you have questions or concerns about the project, please feel free to contact Justin Eccles with AP & Sons or Banner Associates.

BANNER
engineering a better community
