
CLEAR LAKE WATERMAIN AND STORM SEWER PHASE 1A

PROJECT DESCRIPTION

This project consists of watermain and storm sewer improvements, complete street reconstruction including curb & gutter and asphalt pavement, new driveway approach pavement, pedestrian ramp and sidewalk replacement and various removals related to construction of the utilities and street reconstruction.

PROJECT UPDATE | October 20th, 2026



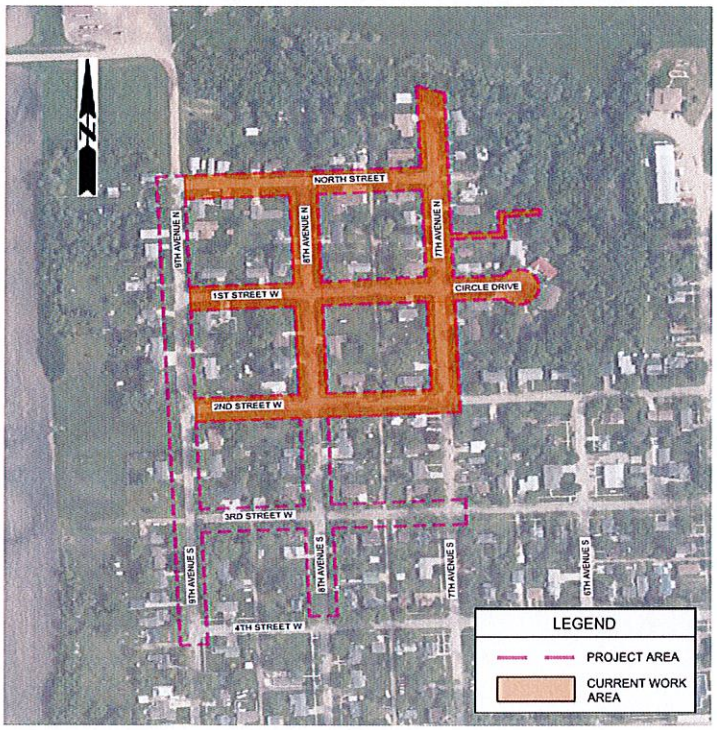

PROJECT INFORMATION

CONSULTANT:

Name: Banner Associates, Inc.
Address: 409 22nd Avenue S, Brookings SD
Phone: 605.692.5714
CONTACT: Landen Buse, Ryan Engstrom, and Scot Leddy

CONTRACTOR:

Name: AP & Sons Construction, Inc
Address: 212 South 6th Street, Milbank SD
Phone 605.520.6647
CONTACT: Justin Eccles

OWNER:

Name: City of Clear Lake
Address: 125 3rd Avenue S, Clear Lake SD
Phone: 605.881.8056
CONTACT: Elliott Furman

PROJECT UPDATE AND SCHEDULE

AP & Sons has completed final gravel grading on 7th between 1st Street and 2nd Street. Banner completed grade checks and proof roll testing, which met project specifications, indicating that area is also ready for asphalt paving. AP & Sons is continuing grading activities in the intersection of 7th and 2nd, as well as 2nd street.

Bowes began paving operations on Friday completing the bottom mat of 7th Avenue from Circle Drive to dead end north of North Street. Bowes will continue paving bottom mat next week. Once bottom mat is completed crew will then work on top mat.

Concrete Crews finished pouring fillets and valley gutters in the intersection of 8th avenue and 2nd Street. After intersection of 7th Avenue and 2nd Street meet the stability and density requirements, fillets and valley gutters will be installed. Once the remaining concrete work is completed, the crew will begin installing concrete driveways.

REMINDER: Residents without alley access can expect temporary restrictions to driveway access while the newly installed asphalt pavement cures. Please use adjacent streets for parking during this time.

BANNER
engineering a better community
