

CLEAR LAKE WATERMAIN AND STORM SEWER PHASE 1A

PROJECT DESCRIPTION

This project consists of watermain and storm sewer improvements, complete street reconstruction including curb & gutter and asphalt pavement, new driveway approach pavement, pedestrian ramp and sidewalk replacement and various removals related to construction of the utilities and street reconstruction.

PROJECT UPDATE | October 27th, 2026

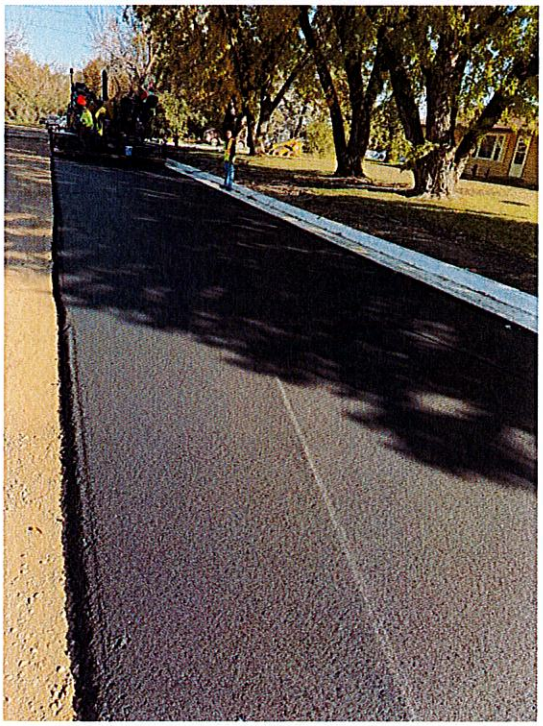

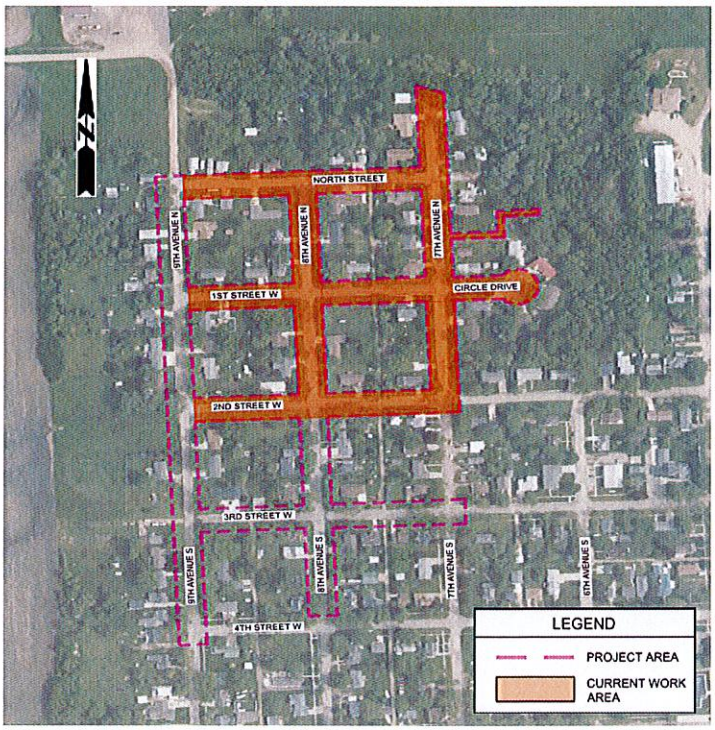

PROJECT INFORMATION

CONSULTANT:
Name: Banner Associates, Inc.
Address: 409 22nd Avenue S, Brookings SD
Phone: 605.692.5714
CONTACT: Landen Buse, Ryan Engstrom, and Scot Leddy

CONTRACTOR:
Name: AP & Sons Construction, Inc
Address: 212 South 6th Street, Milbank SD
Phone 605.520.6647
CONTACT: Justin Eccles

OWNER:
Name: City of Clear Lake
Address: 125 3rd Avenue S, Clear Lake SD
Phone: 605.881.8056
CONTACT: Elliott Furman

PROJECT UPDATE AND SCHEDULE

AP & Sons has finished stabilizing activities in the intersection of 7th and 2nd. Banner completed a proof roll, indicating that area is ready for concrete work. Final grading has been completed on 2nd st W. Banner has completed grade checks and proof rolls, indicating that area is ready for paving

Bowes continued paving operations on Monday, completing the bottom mat of Circle Drive, North Street, 1st street, and 8th ave from North Street to 1st street. Bowes will continue paving bottom mat next week, weather pending. Once bottom mat is completed crew will then work on top mat.

Concrete Crews started pouring fillets in the intersection of 7th avenue and 2nd Street. They will continue installing fillets, and start on valley gutters next week. Once the remaining concrete work is completed, the crew will begin installing concrete driveways.

REMINDER: Residents without alley access can expect temporary restrictions to driveway access while the newly installed asphalt pavement cures. Please use adjacent streets for parking during this time.

BANNER
engineering a better community
